



Architect

Construction Manager



DALEY+JALBOOT
Architects Inc



D'HUY Engineering, Inc.

A TRADITION OF EXCELLENCE

SPRINGFIELD TOWNSHIP MUNICIPAL CAMPUS PROJECT

Springfield Township

DEI Project No. 12069

Monthly Progress Report No. 01

October, 2016

Springfield Township Municipal Campus Project



Phase 2

Phase 2: Buildings and Adjacent Site Work

Start: March 7th, 2016

Completion of Phase: June 23rd, 2017

WORK COMPLETED

Public Works:

- Complete brick at main building and exterior storage building.
- Garage bay slabs placed and second floor concrete topping placed at main building.
- Main building roofing completed.
- Foundations at equipment building completed.
- 80% HVAC duct and units installed.
- Domestic Water, DWV piping, air lines 75% complete.



Public Works Brick Veneer



Police/Admin. Board Room

Police/Admin:

- Structural steel columns and beams completed.
- Exterior metal stud framing completed.
- EPDM roofing system installation in progress.
- Placing duct hangers and coordinating HVAC unit installations.
- Exterior sheathing, cavity insulation and brick in progress.
- Electrical rough-in in progress in stud wall locations. Rough-in at masonry complete.

WORK COMPLETED

Library:


- Footing excavation and footing placement in progress.
- Electric feeds and communication feeds to outside of building footprint complete.
- Structural steel is fabricated and stored off site awaiting delivery.



Library Footings



Equipment building Steel and Masonry

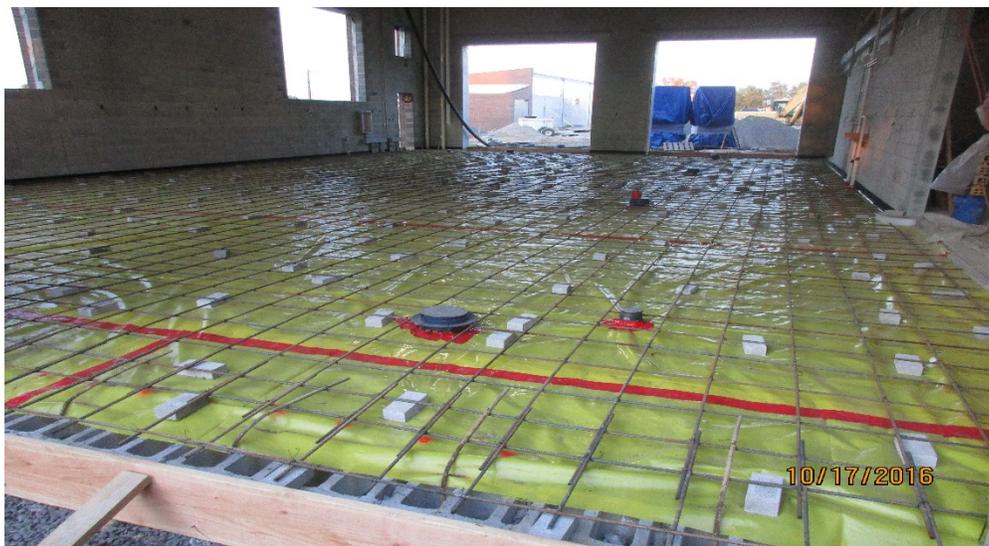

Repair Bay Slab Placement

